


US 35 Corridor Development Status

June 30, 2009

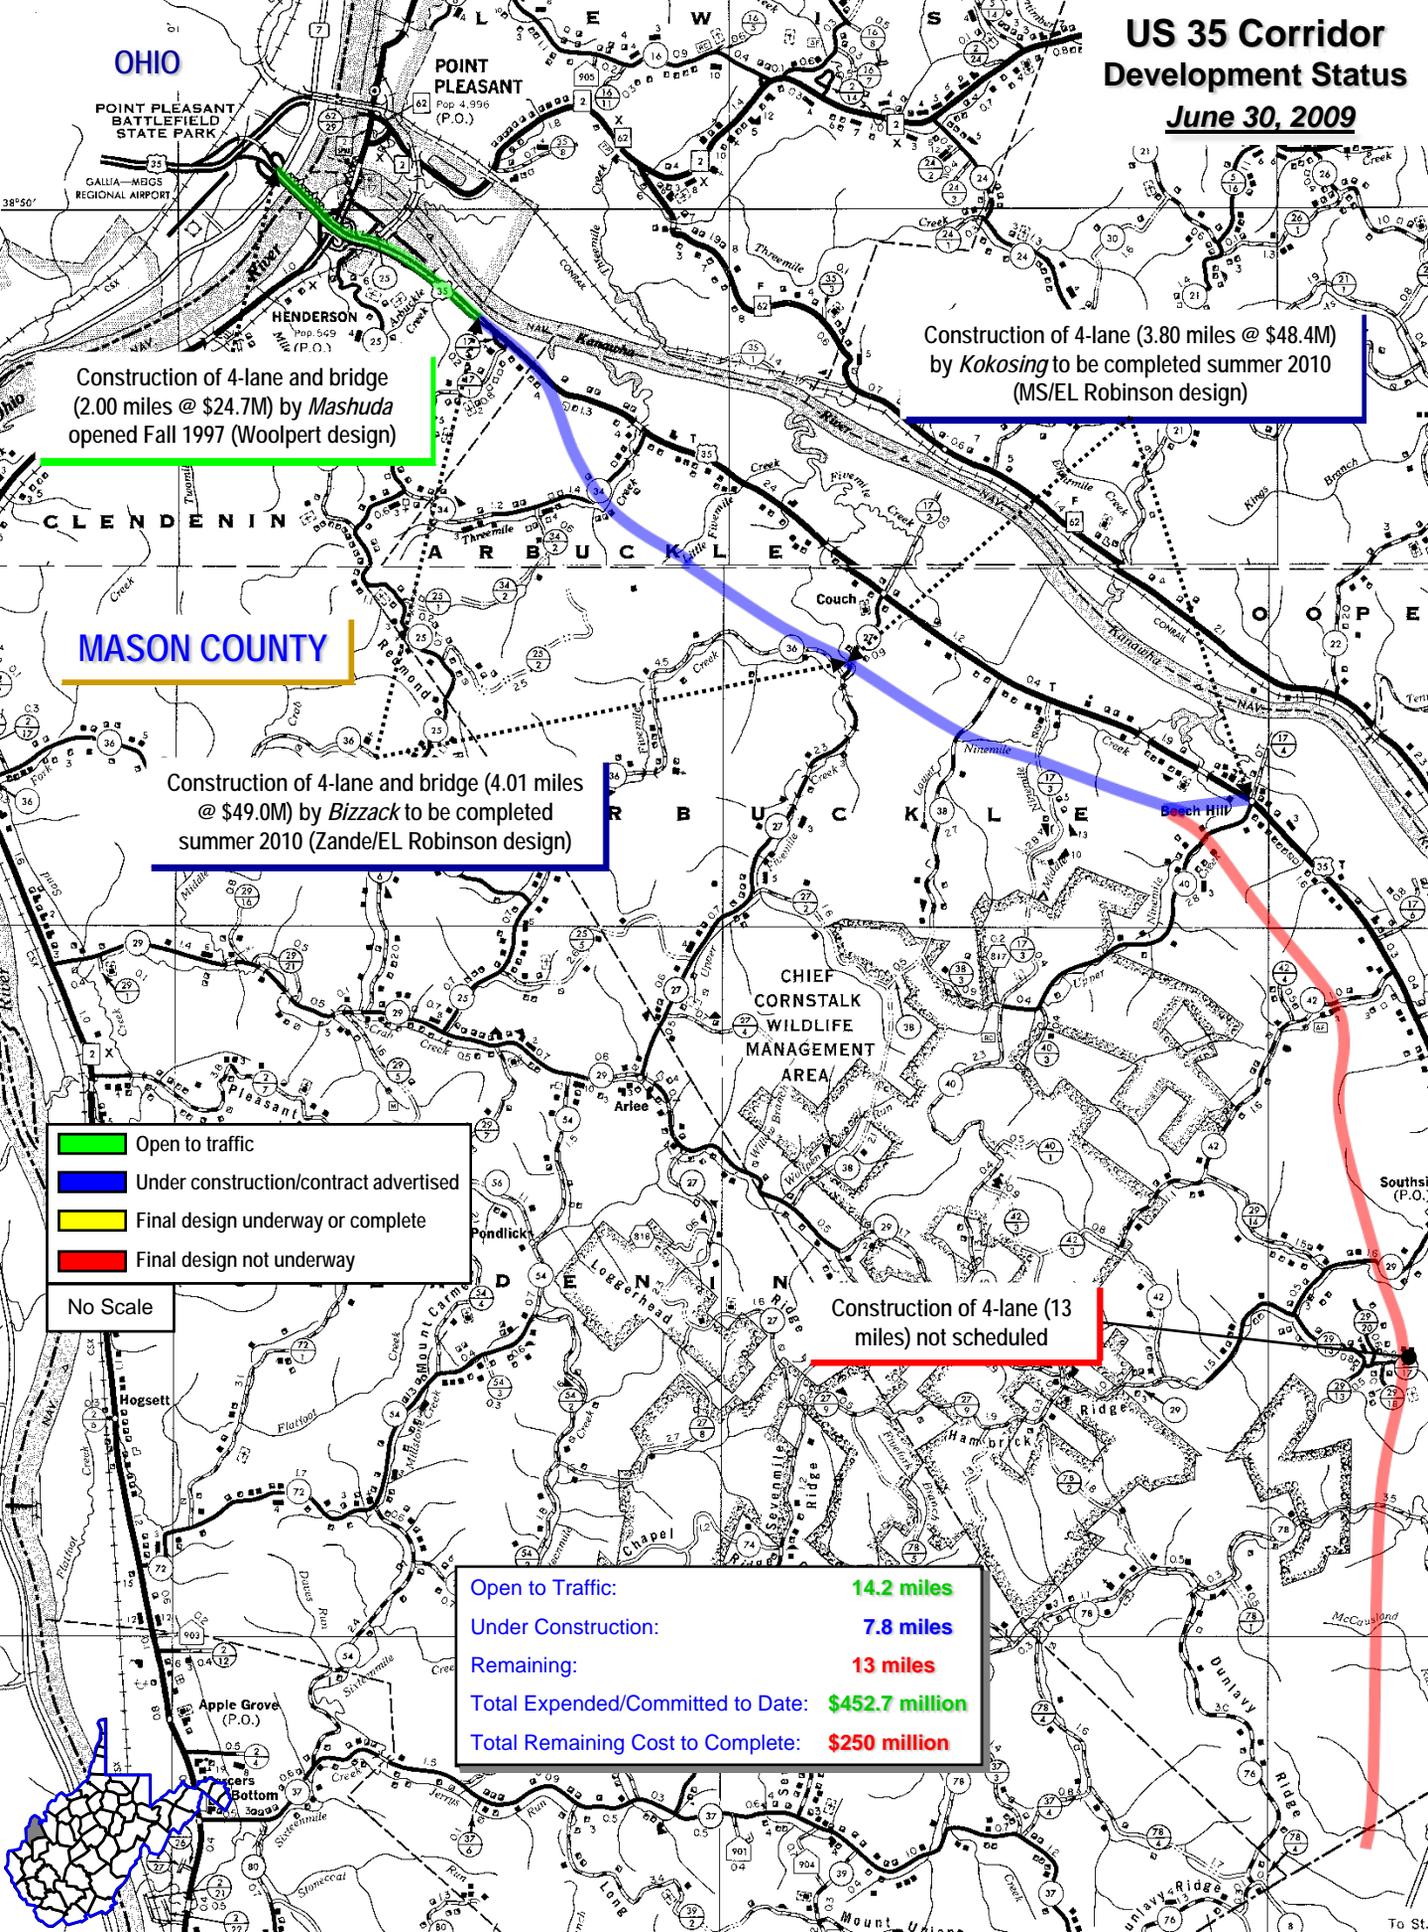

Construction of 4-lane and bridge (2.00 miles @ \$24.7M) by *Mashuda* opened Fall 1997 (Woolpert design)

Construction of 4-lane (3.80 miles @ \$48.4M) by *Kokosing* to be completed summer 2010 (MS/EL Robinson design)

MASON COUNTY

Construction of 4-lane and bridge (4.01 miles @ \$49.0M) by *Bizzack* to be completed summer 2010 (Zande/EL Robinson design)

Construction of 4-lane (13 miles) not scheduled

- Open to traffic
- Under construction/contract advertised
- Final design underway or complete
- Final design not underway

No Scale

Open to Traffic:	14.2 miles
Under Construction:	7.8 miles
Remaining:	13 miles
Total Expended/Committed to Date:	\$452.7 million
Total Remaining Cost to Complete:	\$250 million

